



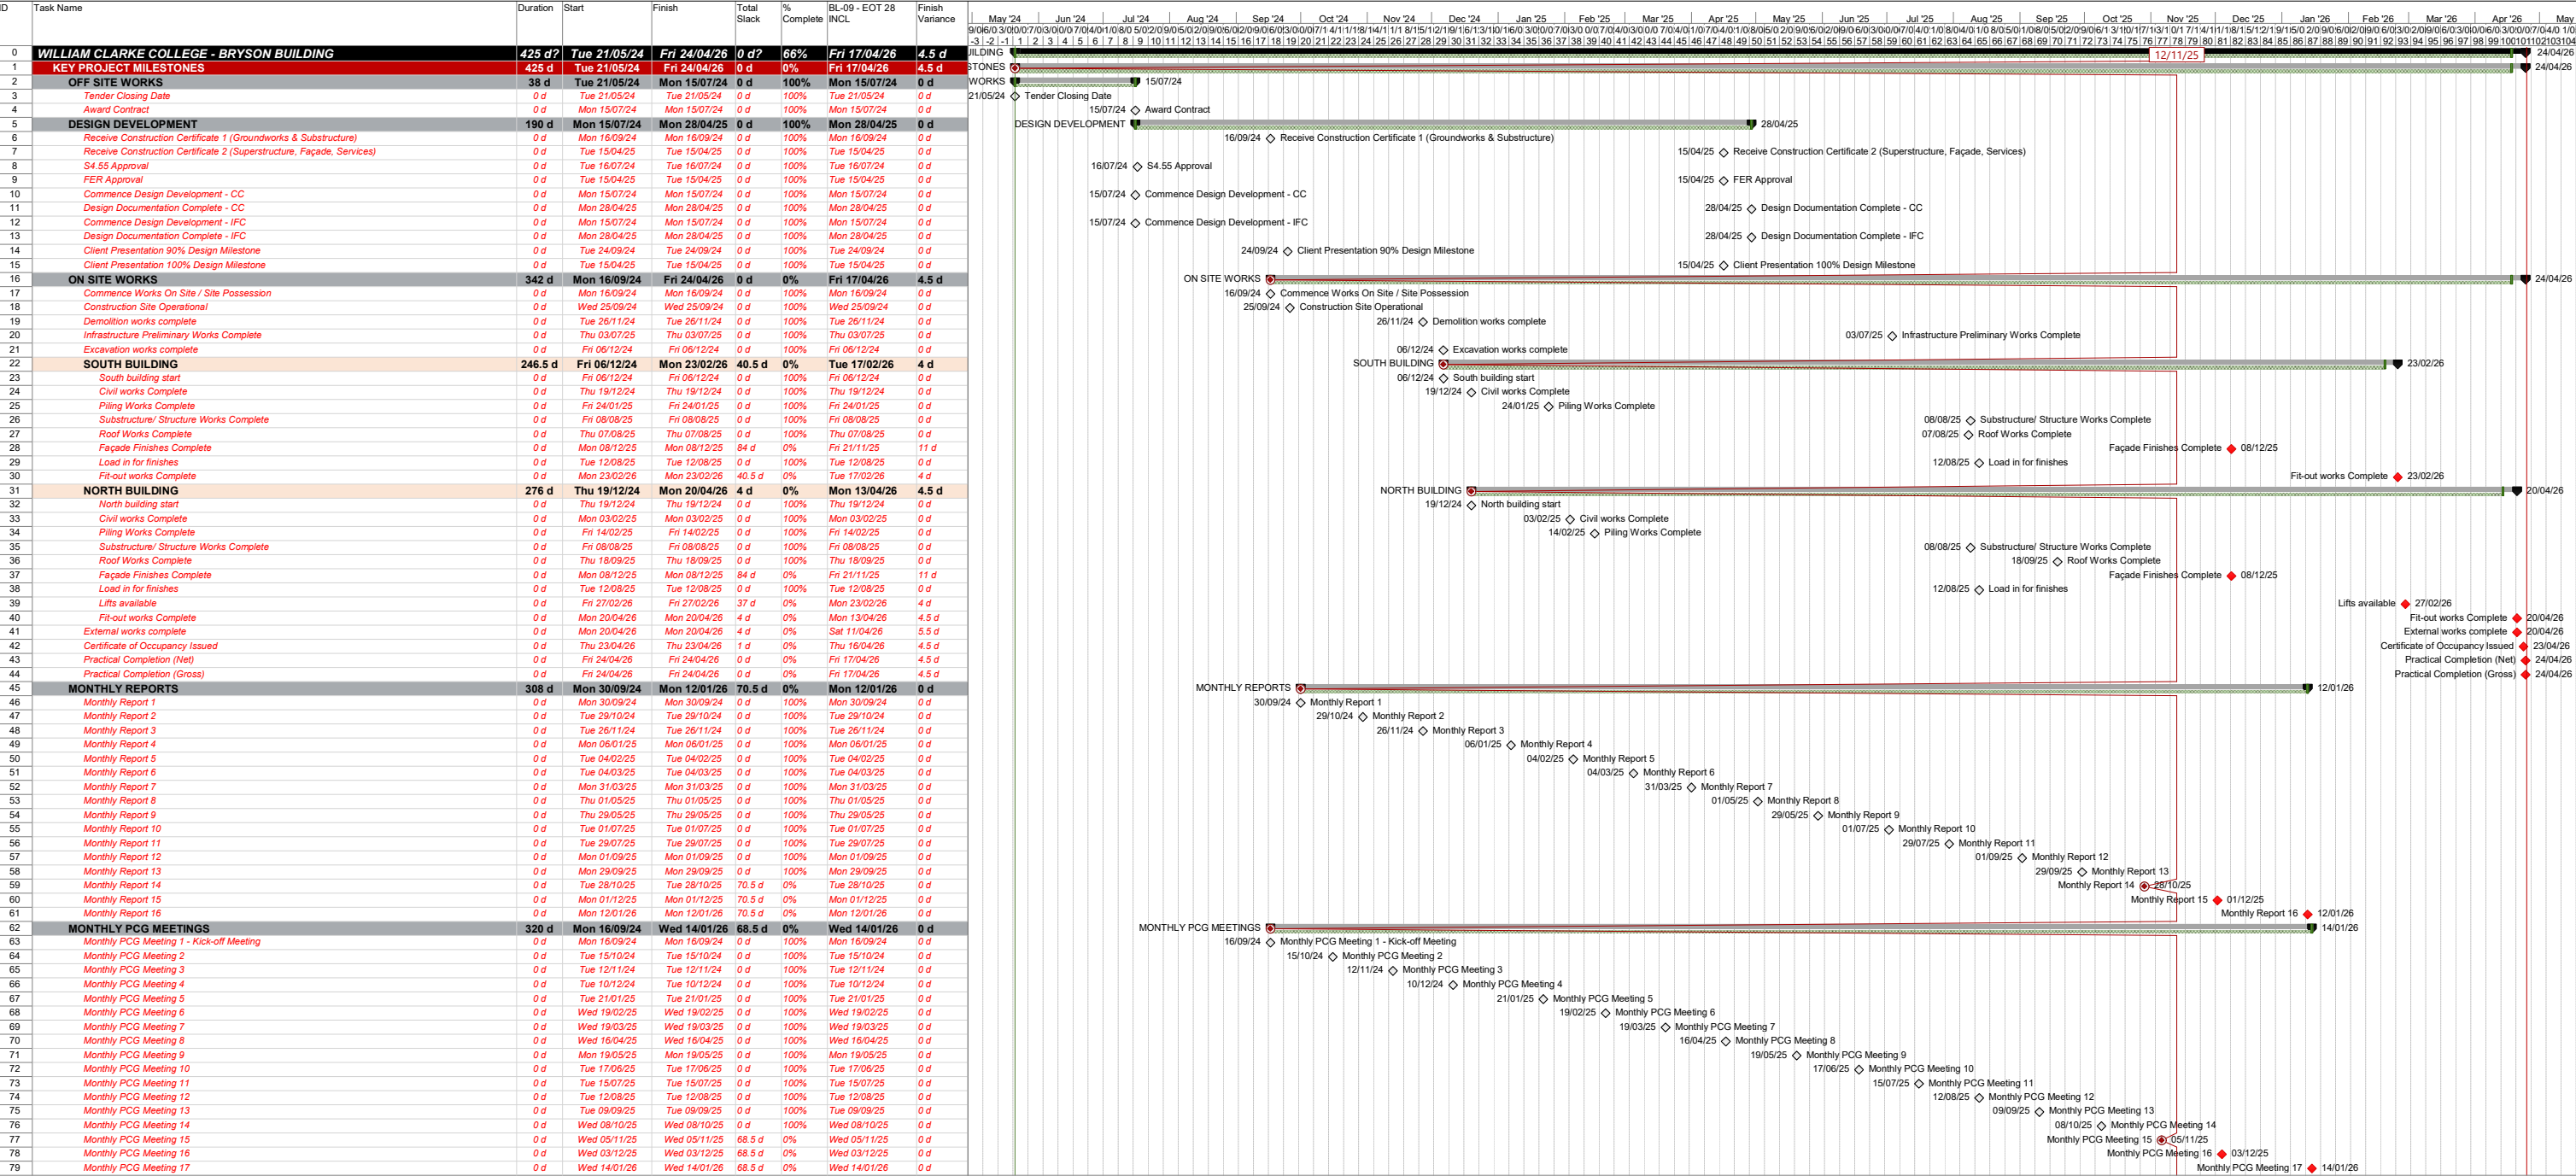

Date: Wed 12/11/2	Critical Task	Milestone	% Complete	Project Summary	Baseline Critical	Baseline Summary
	Non-Critical Tasks	Summary	Completed Milestone	Baseline Normal	Baseline Milestone	
Planned by: MH Checked by: AD						Page 2 of 12
WCC - ROHRIG NSW - STATUS 12.11.25						

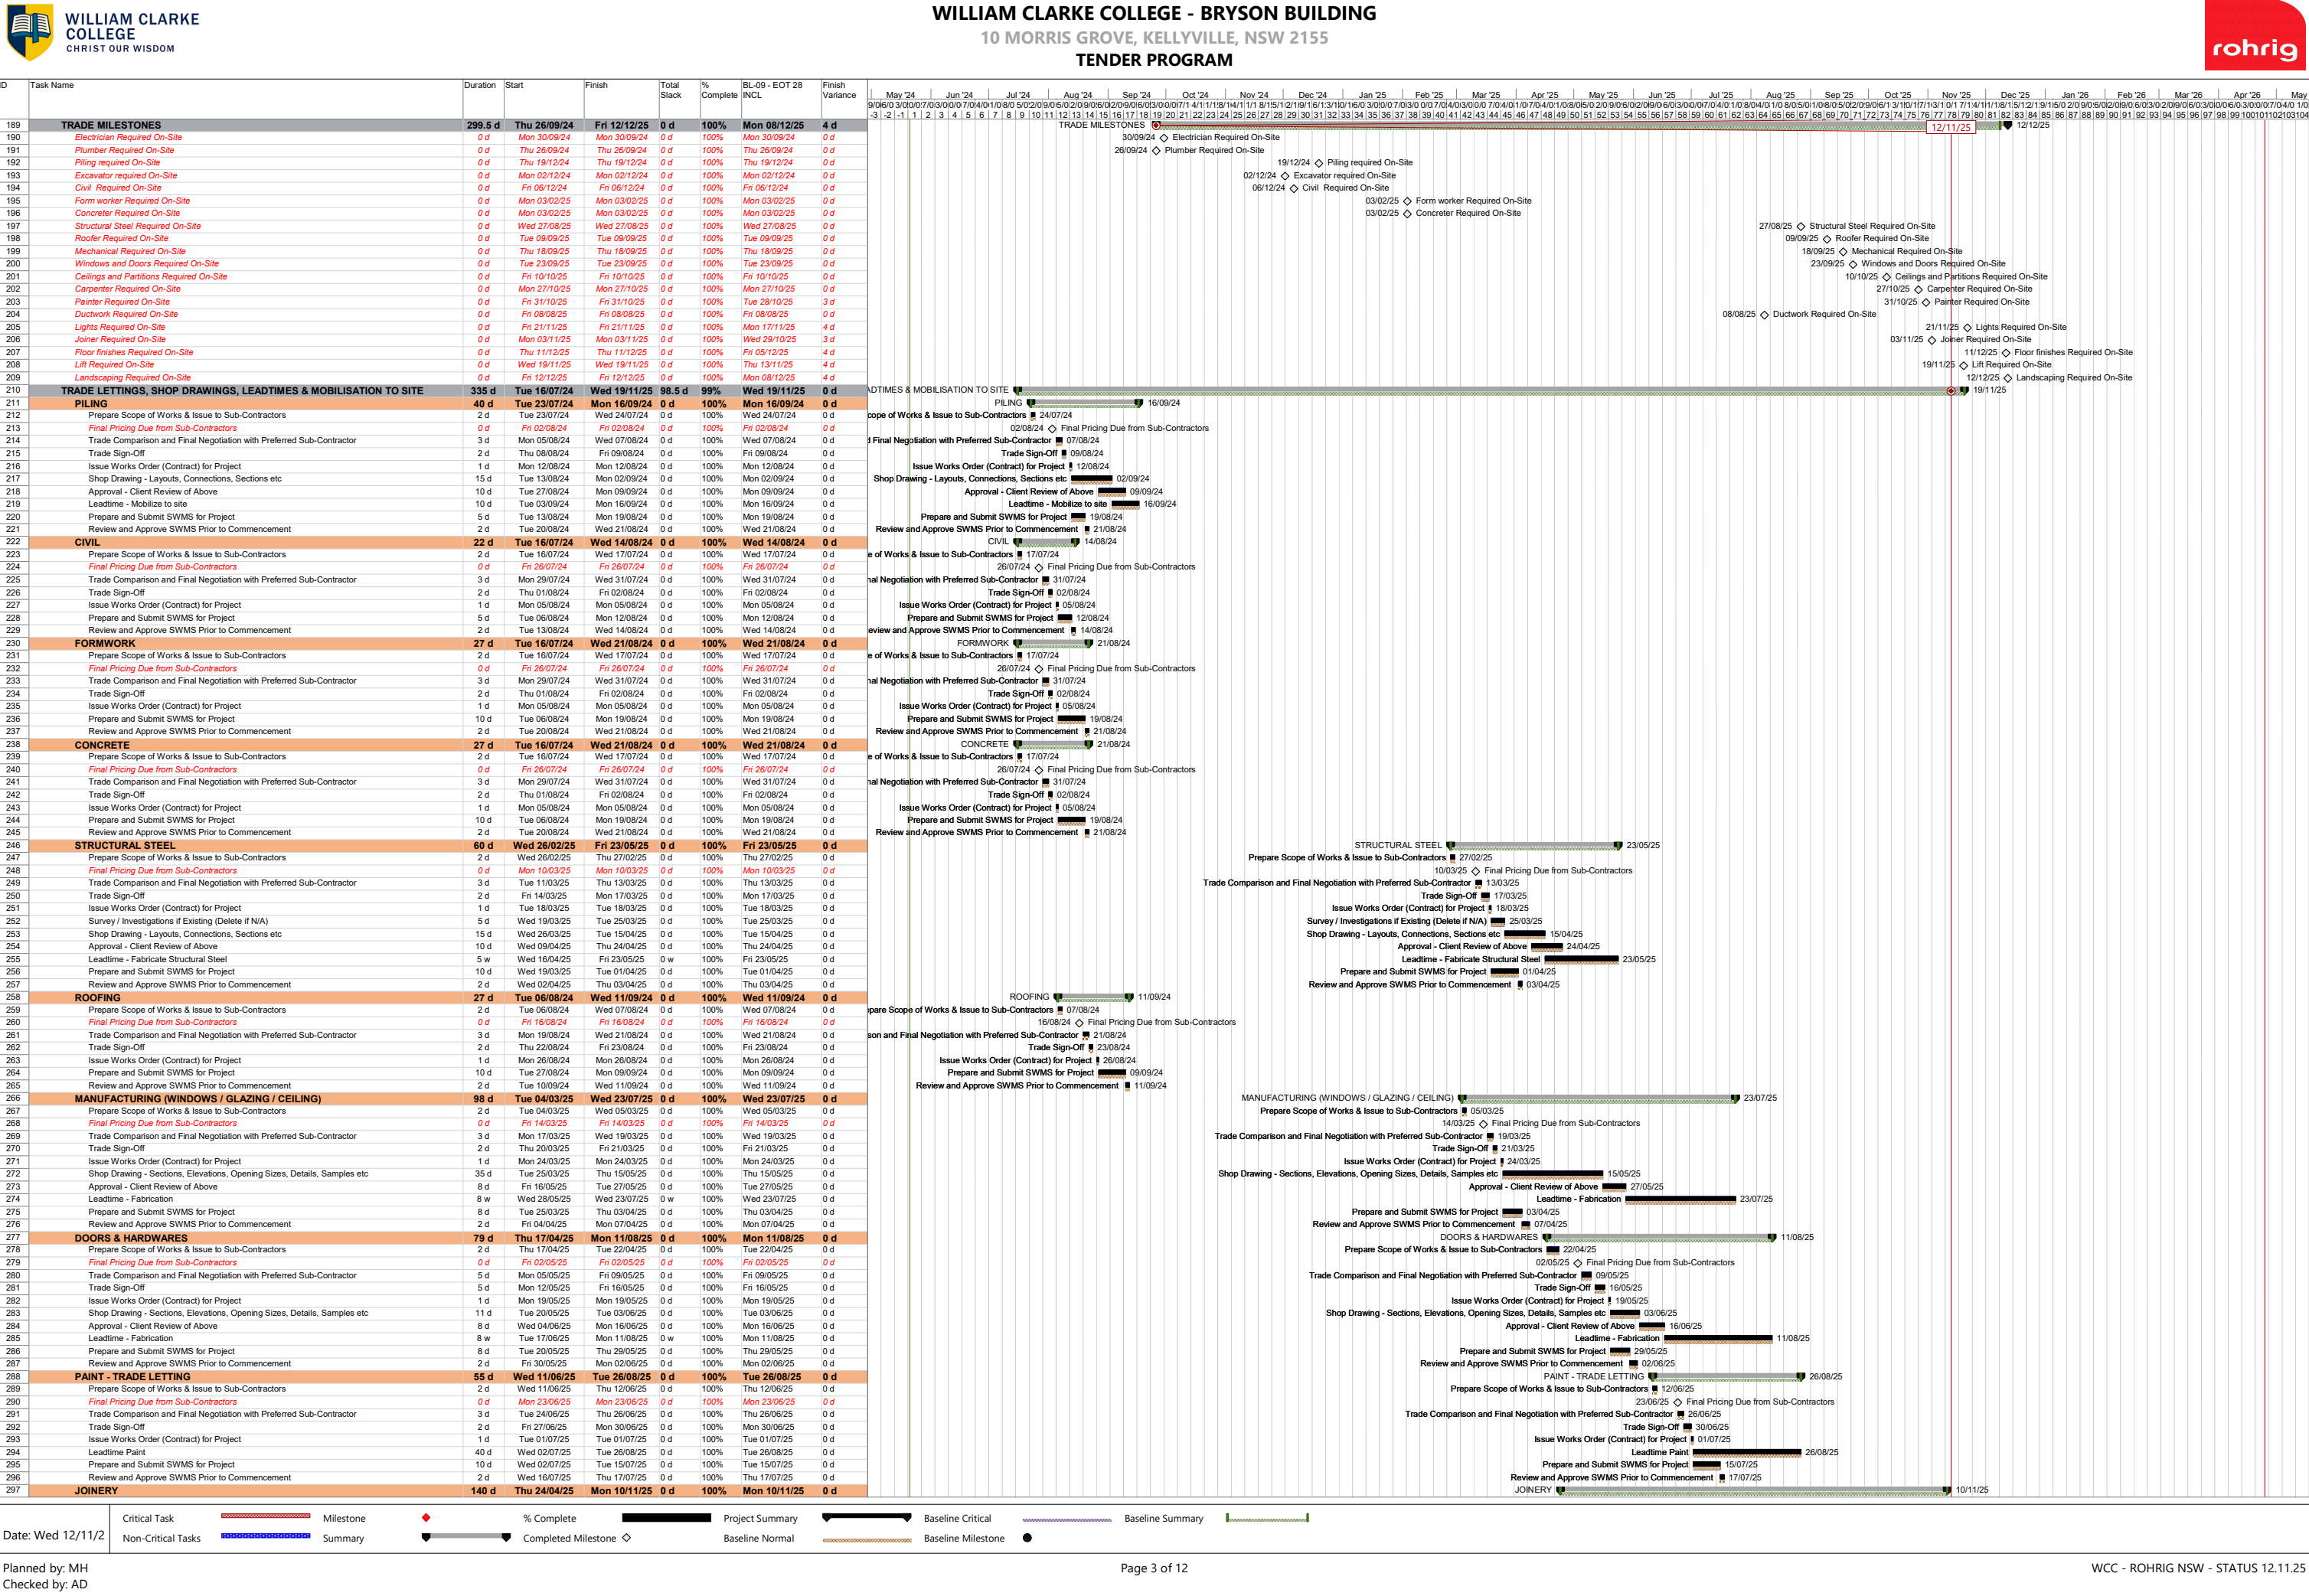

Planned by: MH
 Checked by: AD

Page 4 of 12

WCC - ROHRIG NSW - STATUS 12.11.25

Task Name	Duration	Start	Finish	Total Slack	% Complete	BL-09 - EOT 28 INCL	Finish Variance
407	Data Sheets - Plant Schedule	10 d	Wed 02/07/25	Tue 15/07/25	0 d	100%	Tue 15/07/25
408	Shop Drawings	15 d	Wed 02/07/25	Tue 22/07/25	0 d	100%	Tue 22/07/25
409	Approval - Client Review of Above	10 d	Wed 23/07/25	Tue 05/08/25	0 d	100%	Tue 05/08/25
410	Leadtime - Landscaping	10 w	Wed 06/08/25	Wed 15/10/25	0 w	100%	Wed 15/10/25
411	Prepare and Submit SWMS for Project	10 d	Wed 02/07/25	Tue 15/07/25	0 d	100%	Tue 15/07/25
412	Review and Approve SWMS Prior to Commencement	2 d	Wed 16/07/25	Thu 17/07/25	0 d	100%	Thu 17/07/25
413	Final review SWMS	0 d	Mon 10/11/25	Mon 10/11/25	105.5 d	0%	Mon 10/11/25
414	MATERIALS HANDLING	192 d	Mon 03/02/25	Mon 05/01/26	74 d	78%	Fri 05/12/25
415	TOWER CRANE	192 d	Mon 03/02/25	Mon 05/01/26	74 d	60%	Fri 05/12/25
416	Crane foundation works incl curing	10 d	Mon 03/02/25	Mon 17/02/25	0 d	100%	Mon 17/02/25
417	CRANE DURATION ON SITE	182 d	Tue 18/02/25	Mon 05/01/26	74 d	33%	Fri 05/12/25
418	Crane Installation	5 d	Tue 18/02/25	Mon 24/02/25	0 d	100%	Mon 24/02/25
419	Crane removal	5 d	Mon 08/12/25	Mon 15/12/25	21 d	0%	Fri 28/11/25
420	Crane removed	0 d	Mon 15/12/25	Mon 15/12/25	21 d	0%	Fri 28/11/25
421	Scar works	5 d	Mon 15/12/25	Mon 05/01/26	74 d	0%	Fri 05/12/25
422	SCAFFOLDING	162 d	Mon 10/03/25	Fri 12/12/25	0 d	100%	Thu 27/11/25
423	Scaffolding - L1 to L2	4 d	Mon 10/03/25	Fri 14/03/25	0 d	100%	Fri 14/03/25
424	Scaffolding - L2 to L3	4 d	Fri 02/05/25	Thu 08/05/25	0 d	100%	Thu 08/05/25
425	Scaffolding - L3 to L4	4 d	Thu 29/05/25	Thu 05/06/25	0 d	100%	Thu 05/06/25
426	Scaffolding - L4 to Roof	4 d	Thu 29/05/25	Thu 05/06/25	0 d	100%	Thu 05/06/25
427	Scaffold dismantling	4 d	Mon 08/12/25	Fri 12/12/25	0 d	100%	Thu 27/11/25
428	Remove scaffolds	0 d	Fri 12/12/25	Fri 12/12/25	0 d	100%	Thu 27/11/25
429	Material Handling Complete	0 d	Mon 05/01/26	Mon 05/01/26	0 d	100%	Fri 05/12/25

May '24Jun '24Jul '24Aug '24Sep '24Oct '24Nov '24Dec '24Jan '25Feb '25Mar '25Apr '25May '25Jun '25Jul '25Aug '25Sep '25Oct '25Nov '25Dec '25Jan '26Feb '26Mar '26Apr '26May '26

0000300007703000770401080150220905020806050300

Date: Wed 12/11/2	Critical Task	Milestone	% Complete	Project Summary	Baseline Critical	Baseline Summary
	Non-Critical Tasks	Summary	Completed Milestone	Baseline Normal	Baseline Milestone	
Planned by: MH Checked by: AD						Page 6 of 12
WCC - ROHRIG NSW - STATUS 12.11.25						

Date: Wed 12/11/2

Critical Task  Milestone  % Complete  Project Summary  Baseline Critical  Baseline Summary

Non-Critical Tasks Summary Completed Milestone Baseline Normal Baseline Milestone

Date: Wed 12/11/2
 Critical Task Milestone % Complete Project Summary Baseline Critical Baseline Summary
 Non-Critical Tasks Summary Completed Milestone Baseline Normal Baseline Milestone

Date: Wed 12/11/2

Critical Task

Non-Critical Tasks

Milestone

Summary

% Complete

Completed Milestone

Project Summary

Baseline Normal

Baseline Critical

Baseline Milestone

Baseline Summary

Planned by: MH

Checked by: AD

Page 10 of 12

WCC - ROHRIG NSW - STATUS 12.11.2

Date: Wed 12/11/2

Critical Task	Milestone	% Complete	Project Summary	Baseline Critical	Baseline Summary
Non-Critical Tasks	Summary	Completed Milestone	Baseline Normal	Baseline Milestone	

