



William Clarke College Bryson Building
Monthly Project Update
MAY 2025

Prepared by:
Rohrig (NSW) Pty Ltd
Lot 13, 133-137 Beauchamp Road
Matraville NSW 2036

Prepared for:
William Clarke College
1 Morris Grove
Kellyville NSW 2155

WORKS COMPLETED THIS MONTH

- Structure
 - Level 2 to 3 verticals (columns and walls) poured
 - Level 3 to 4 verticals (columns and walls) poured
 - Level 3 slab Pour 1, 2, and 3 complete
 - Level 4 slab Pour 1 complete
 - Level 4 slab Pour 2 and 3 formwork and reinforcement commenced
- Electrical
 - Penetrations to level 4 slab
- Hydraulic
 - Penetrations to level 4 slab
- Fire
 - Penetrations to level 4 slab
- Scaffolding
 - Level 3 Perimeter scaffold installed
 - Level 4 scaffold commenced

WORKS PLANNED NEXT MONTH

- Structure
 - Formwork, Reinforcement, Pour to Level 4 Pour 2 and Pour 3
 - Post Tension to Level 4 Pour 2 and Pour 3
 - Concrete Pour verticals Level 3-4 Pour 2 and Pour 3, Level 4 Pour 1, Pour 2 and Pour 3
 - Structural Steel installation to roof level
 - Stripping of formwork Level 1-4 Pour 1, Pour 2, Pour 3
- Electrical
 - Commence rough in Electrical Services
- Hydraulic
 - Commence rough in Hydraulic Services
- Mechanical
 - Commence rough in Mechanical Services
- Fire
 - Commence rough in Fire Services
- Scaffolding to roof Level
- Façade
 - Façade setout and secondary steel installation
- Finishes
 - Commencement of waterproofing
 - Setouts for internal works

PROGRESS PHOTOS

Photos From Daily Log

Description

Taken date

29/5/2025 at 10:39 am

Upload date

29/5/2025 at 10:45 am

Uploaded by

Michael Wilson

File name

[1748479491545.25293...](#)



Photos From Daily Log

Description

Taken date

27/5/2025 at 09:25 am

Upload date

27/5/2025 at 09:32 am

Uploaded by

Michael Wilson

File name

[1748302309403.67602...](#)



Photos From Daily Log

Description

Taken date

26/5/2025 at 01:43 pm

Upload date

26/5/2025 at 01:44 pm

Uploaded by

Michael Lucas

File name

[EDEEDE26-4873-46E7-A...](#)



Photos From Daily Log

Description

Taken date

24/5/2025 at 12:35 pm

Upload date

24/5/2025 at 12:36 pm

Uploaded by

Michael Lucas

File name

[DB26816F-8266-4CF0-A...](#)



Photos From Daily Log

Description

Taken date

24/5/2025 at 12:28 pm

Upload date


24/5/2025 at 12:30 pm

Uploaded by

Michael Lucas

File name

[DB932AB5-1F0C-4741-9...](#)

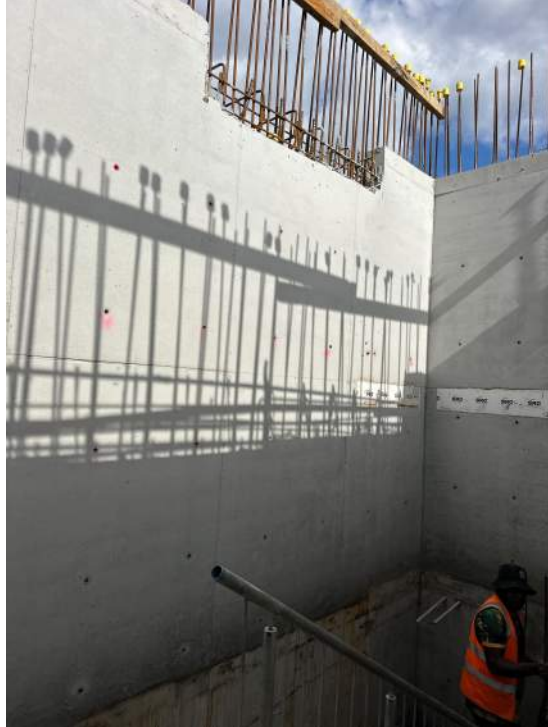

Photos From Daily Log

Description

Taken date

19/5/2025 at 12:55 pm

Upload date

19/5/2025 at 12:55 pm

Uploaded by

Michael Lucas

File name

[304744FE-1371-489F-B...](#)



Photos From Daily Log

Description

Taken date

19/5/2025 at 12:53 pm

Upload date

19/5/2025 at 12:54 pm

Uploaded by

Michael Lucas

File name

6E9F488A-D745-48D8-B...



Photos From Daily Log

Description

Taken date

12/5/2025 at 02:47 pm

Upload date

12/5/2025 at 02:47 pm

Uploaded by

Michael Lucas

File name

263F7068-B445-4451-A...



Photos From Daily Log

Description

Taken date

8/5/2025 at 04:13 pm

Upload date

8/5/2025 at 04:14 pm

Uploaded by

Michael Lucas

File name

[DBF3A822-FA2D-491C-A...](#)



Photos From Daily Log

Description

Taken date

6/5/2025 at 04:16 pm

Upload date


6/5/2025 at 04:22 pm

Uploaded by

Michael Lucas

File name

[8C064D50-FC57-4575-9...](#)

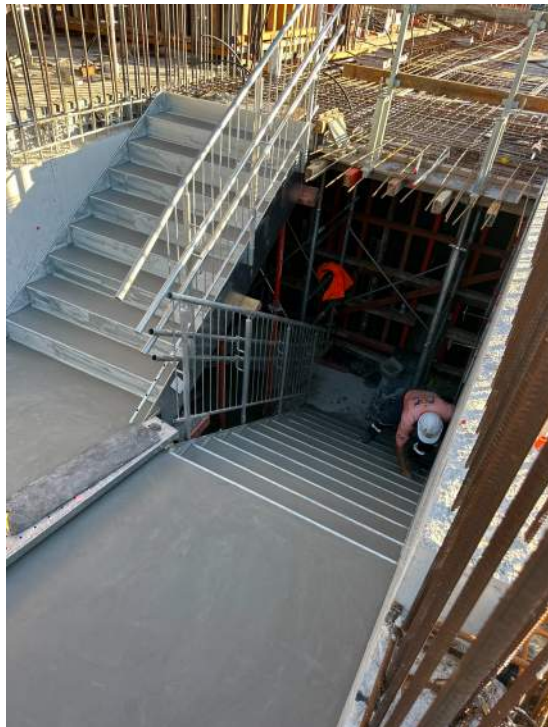

Unclassified

Description
LEVEL 3 POUR 2 PT

Taken date
5/5/2025 at 12:39 pm

Upload date
5/5/2025 at 12:39 pm

Uploaded by
Joshua Gosling

File name
[40AFF309-6157-44B4-9...](#)



Unclassified

Description
LEVEL 3 POUR 3

Taken date
5/5/2025 at 12:38 pm

Upload date
5/5/2025 at 12:38 pm

Uploaded by
Joshua Gosling

File name
[04EC7C8E-52D0-4170-8...](#)



Site photos

Description

Taken date

1/5/2025 at 02:09 pm

Upload date

1/5/2025 at 02:20 pm

Uploaded by

Andries Van Der Walt

File name

62CCD2C6-91D8-4A48-...

