



William Clarke College Bryson Building

Monthly Project Update
JUNE 2025

Prepared by: Rohrig (NSW) Pty Ltd Lot 13, 133-137 Beauchamp Road Matraville NSW 2036 **Prepared for:**William Clarke College
1 Morris Grove
Kellyville NSW 2155

WORKS COMPLETED THIS MONTH

- Structure
 - o Level 4 Pour 3 formwork and reinforcement complete
 - o Level 4-roof columns complete
 - o Formwork stripping complete to Level 1-4 Pour 1
 - o Formwork stripping commenced Level 1-4 Pour 2
- Electrical
 - o Commenced rough in of electrical services
- Hvdraulic
 - o Commenced rough in of hydraulic services
- Mechanical
 - o Commenced rough in of mechanical services
- Fire
 - o Commenced rough in of fire services
- Finishes
 - o Internal set out and wall framing commenced
- Façade
 - o Commencement of façade set out and secondary steel installation
- Scaffolding
 - o Perimeter scaffold complete
 - o Roof scaffolding commenced

WORKS PLANNED NEXT MONTH

- Structure
 - o Pour slab to Level 4 pour 3
 - o Pour verticals to Level 3 4 pour 3
 - o Structural Steel installation to roof level
 - o Stripping of formwork Level 1-4 Pour 2, Pour 3
- Electrical
 - o Rough in Electrical Services
- Hydraulic
 - o Rough in Hydraulic Services
- Mechanical
 - o Rough in Mechanical Services
- Fire
 - o Rough in Fire Services
- Scaffolding
 - o Completion of roof scaffold
- Façade
 - o Façade setout and secondary steel installation
 - o Commencement of external cladding
 - Commencement of roofing
 - Commencement of blockwork
- Finishes
 - Commencement of waterproofing
 - Commencement of painting
 - Setouts for internal works
 - Wall framing

PROGRESS PHOTOS



Photos From Daily Log


Description

Taken date 27/6/2025 at 09:45 am

Upload date 27/6/2025 at 09:45 am

Uploaded by Michael Wilson

File name 1F8EF278-0096-49C6-8...

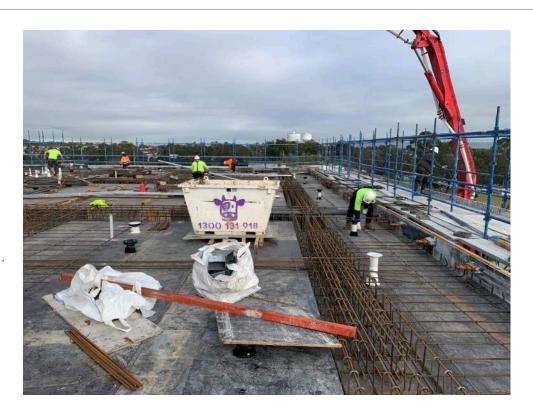

internals level 2

Description

Taken date 25/6/2025 at 03:23 pm

Upload date 25/6/2025 at 05:43 pm

Uploaded by James Watson

File name A5A193B7-DD86-4192-B...





Site photos


Description

Taken date 25/6/2025 at 02:18 pm

Upload date 25/6/2025 at 02:18 pm

Uploaded by Michael Wilson

File name 627AB985-6BD8-4E77-9...

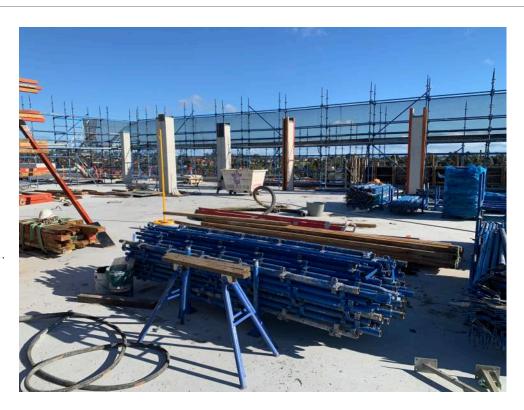

internals level 1


Description

Taken date 25/6/2025 at 09:12 am

Upload date 25/6/2025 at 09:26 am

Uploaded by James Watson

File name AEE88295-FFE1-4102-8...

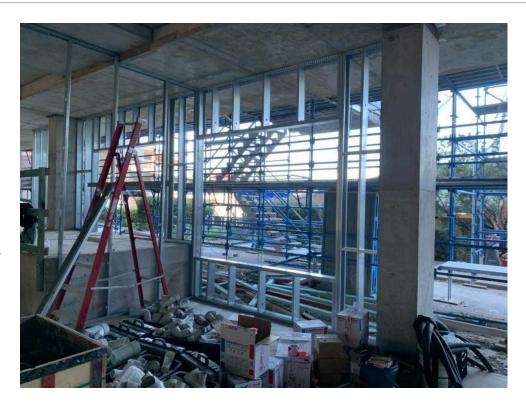



internals level 1

Description

Taken date 25/6/2025 at 09:11 am

Upload date 25/6/2025 at 09:12 am

Uploaded by James Watson

File name AF99D4DE-C45C-48FF-8...



internals level 1


Description

Taken date 24/6/2025 at 09:44 am

Upload date 24/6/2025 at 09:45 am

Uploaded by James Watson

File name 2617B1B9-7C33-4599-8...

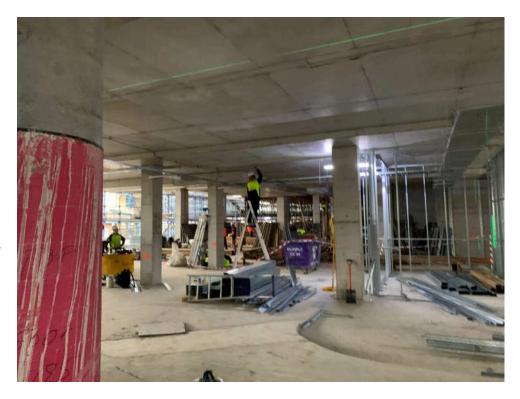



internals level 2

Description

Taken date 24/6/2025 at 09:41 am

Upload date 24/6/2025 at 09:41 am

Uploaded by James Watson

File name 78982850-97F9-42FF-8...



internals level 1

Description

Taken date 23/6/2025 at 01:11 pm

Upload date 23/6/2025 at 01:12 pm

Uploaded by James Watson

File name 030E61FF-0F58-41AE-A...





Unclassified

Description

Taken date 23/6/2025 at 01:05 pm

Upload date 23/6/2025 at 01:09 pm

Uploaded by James Watson

File name 87B7FC48-4106-446A-9...

