

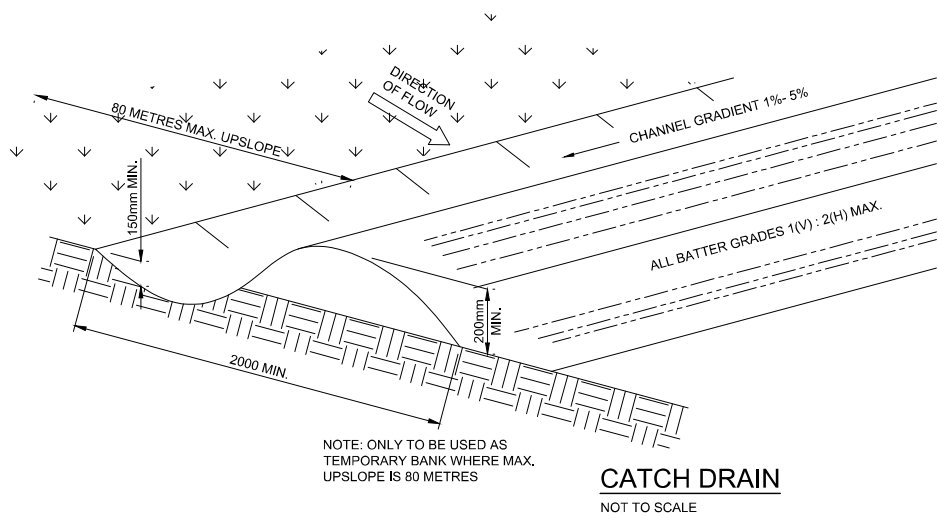


- STOCKPILE CONSTRUCTION NOTES:**
1. PLACE STOCKPILES MORE THAN 2 (PREFERABLY 5) METRES FROM EXISTING VEGETATION, CONCENTRATED WATER FLOW, ROADS AND HAZARD AREAS.
  2. CONSTRUCT ON THE CONTOUR AS LOW, FLAT, ELONGATED MOUNDS.
  3. WHERE THERE IS SUFFICIENT AREA, TOPSOIL STOCKPILES SHALL BE LESS THAN 2 METRES IN HEIGHT.
  4. WHERE THEY ARE TO BE PLACED FOR MORE THAN 10 DAYS, STABILISE FOLLOWING THE APPROVED E.S.C.P. OR S.W.M.P. TO REDUCE THE C-FACTOR TO LESS THAN 0.10.
  5. CONSTRUCT EARTH BANKS ON THE UPSLOPE SIDE TO DIVERT WATER AROUND STOCKPILES AND SEDIMENT FENCES 1 TO 2 METRES DOWNSLOPE.



- CATCH DRAIN CONSTRUCTION NOTES:**
1. CONSTRUCT ALONG GRADIENT AS SPECIFIED.
  2. MAXIMUM SPACING BETWEEN BANKS SHALL BE 80 METRES.
  3. DRAINS TO BE OF PARABOLIC OR TRAPEZOIDAL CROSS SECTION NOT V-SHAPED.
  4. EARTH BANKS TO BE ADEQUATELY COMPACTED IN ORDER TO PREVENT FAILURE.
  5. CONSTRUCTION OF A TEMPORARY NATURE AND SHALL BE COMPACTED AT THE END A DAYS WORK OR IMMEDIATELY PRIOR RAIN.
  6. ALL OUTLETS FROM DISTURBED LANDS ARE TO FEED INTO SEDIMENT BASIN OR SIMILAR.
  7. DISCHARGE RUNOFF COLLECTED FROM UNDISTURBED LANDS ONTO EITHER A STABILISED OR AN UNDISTURBED DISPOSAL SITE WITHIN THE SAME SUBCATCHMENT AREA FROM WHICH THE WATER ORIGINATED.
  8. COMPACT WITH A SUITABLE IMPLEMENT IN SITUATIONS WHERE THEY ARE REQUIRED TO FUNCTION FOR MORE THAN 5 DAYS.
  9. EARTH BANKS TO BE FREE OF PROJECTIONS OR OTHER IRREGULARITIES THAT WILL IMPEDE NORMAL FLOW.

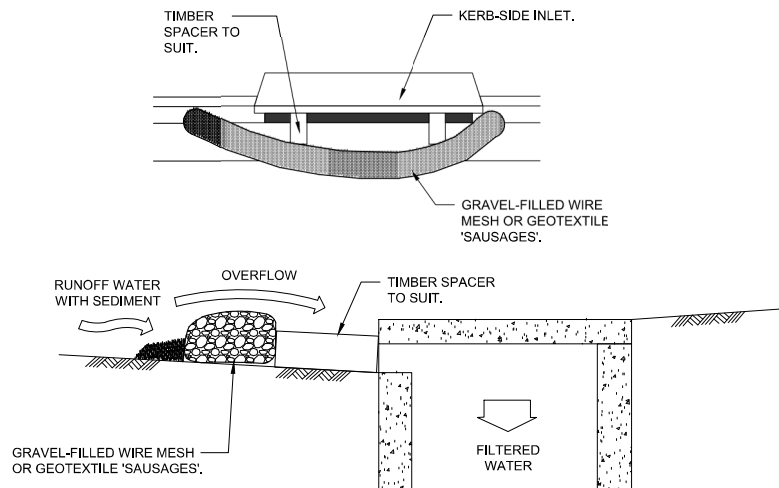

- NOTES:**
1. FABRICATE A SLEEVE MADE FROM GEOTEXTILE OR WIRE MESH LONGER THAN THE LENGTH OF THE INLET PIT AND FILL IT WITH 25mm TO 50mm GRAVEL.
  2. FORM AN ELLIPTICAL CROSS-SECTION ABOUT 150mm HIGH Ax 400mm WIDE.
  3. PLACE THE FILTER AT THE OPENING LEAVING AT LEAST A 100mm SPACE BETWEEN IT AND THE KERB INLET. MAINTAIN THE OPENING WITH SPACER BLOCKS.
  4. FORM A SEAL WITH THE KERB TO PREVENT SEDIMENT BYPASSING THE FILTER.
  5. SANDBAGS FILLED WITH GRAVEL CAN SUBSTITUTE FOR THE MESH OR GEOTEXTILE PROVIDING THEY ARE PLACED SO THAT THEY CAN FIRMLY ABUT EACH OTHER AND SEDIMENT/LADEN WATERS CANNOT PASS BETWEEN.

**PRELIMINARY ISSUE**  
NOT FOR CONSTRUCTION

A		ISSUE FOR TENDER	05.04.24
ISSUE	DESCRIPTION	APPROVED	DATE
ARCHITECT		PMDL	
INTERIORS		MASTERPLANNING	
PMDL ARCHITECTURE + DESIGN PTY LTD ABN 66 062 841 217		PMDL ARCHITECTURE + DESIGN PTY LTD ABN 66 062 841 217	
NSW NOMINATED ARCHITECTS: ANDREW PENDER 0017 DAVID MORRIS 0088 VICK VAN DIJK 0476			

<b>BIRZULIS ASSOCIATES</b>		CONSULTING STRUCTURAL & CIVIL ENGINEERS	
583 DARLING STREET ROZELLE NSW 2039		tel: (02) 9555 7230 email: office@birzulisassociates.com	
PROJECT		WILLIAM CLARKE COLLEGE	
10 MORRIS GROVE, KELLYVILLE		- BRYSON BUILDING	
TITLE		SOIL EROSION AND SEDIMENT CONTROL DETAILS	
SCALES	as noted @ A1	DATE	JULY 2023
DRAWN	C,KE	DESIGN	GK/MG
VERIFIED		APPROVED	
This drawing is the copyright of Birzulis Associates Pty Ltd and may not be altered, reproduced or transmitted in any form or by any means, in part or in whole without the written permission of Birzulis Associates Pty Ltd.			
All levels and dimensions are to be checked and verified on site prior to the commencement of any work, making of also drawings or fabrication of components. Do not scale drawings. Use figure dimensions.			
ISSUE	PROJECT No.	DRAWING No.	
A	8932	C.11	
